
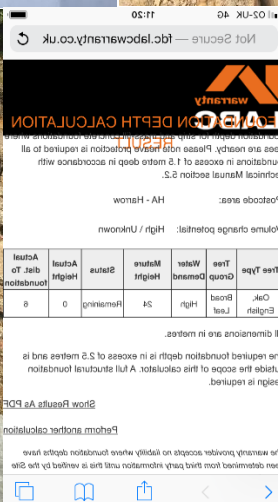


SITE INSPECTION RECORD FORM

PROJECT:	161 Park Avenue, Ruislip, HA4 7UN	JOB REF:	3675
PROJECT MANAGER	Geoff Wilkinson	DATE:	05/06/2019
INSPECTION PLAN			
No of Inspections required 7 This is inspection No 1 of 7 Inspections Further Inspections Still Required 6__			
INSPECTION STAGE & TYPE:			
<input type="checkbox"/> 1 - Commencement	<input type="checkbox"/> 2 - Excavation Works	<input type="checkbox"/> 3 - Below Ground Drainage	<input type="checkbox"/> 4 - Site Preparation
<input type="checkbox"/> 5 - Structural Works	<input type="checkbox"/> 6 - Internal Plumbing	<input type="checkbox"/> 7 - Fire Safety Works	<input type="checkbox"/> 8 - Access & Use
<input type="checkbox"/> 9 - 28 Day progress	<input type="checkbox"/> 10 - Insulation	<input type="checkbox"/> 11 - Testing	<input type="checkbox"/> 12 - Completion
CONTACT DETAILS: Contact Number			
Met with builder and Umesh on site to look at foundations.			
Due to an oak tree approximately 7 m away from foundation area, foundation had been taken down to 2.5 m as per structural design shown on site. At midpoint of foundation excation to step up to 2.1m and to front of building to step up to 1.5m.			
Due to size of foundation 2.5m sections to be poured first then other sections, asked for all foundations to be tied together. Soil conditions was Sandy clay.			
Shuttering had been placed to some parts, asked for photographs to be sent across of all outstanding areas to be reviewed.			

PHOTOS

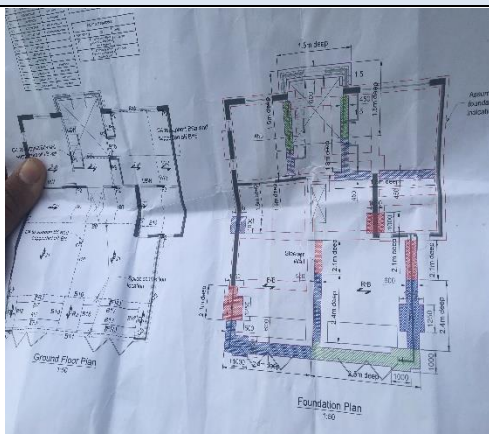

NONCONFORMITY(S) TO BE ACTIONED
CLIENT TO BE NOTIFIED BY EMAIL

(OR COPY LEFT ON SITE)



DATE NEXT INSPECTION BOOKED: TBR (Max 28 days) OR WORKS COMPLETE ISSUE FINAL CERTIFICATE

Note: This inspection report is restricted to requirements covered by Building Regulations current at that time. It does not constitute evidence that the Building Regulations have been satisfied until a Completion/Final Certificate has been issued for the project. It remains the responsibility of the person carrying out the work to ensure that the work complies with the Building Regulations.

SURVEYORS SIGNATURE :



Wayne Smith
