

Protective Fencing

To be erected prior to the commencement of all works on site, and retained in place throughout construction.
To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-tamper couplers, installed so that they can only be removed from inside the fence. The panels should be supported on the inner side by stabilizer struts, which should be attached to a base plate and secured with ground pins.
All weather notices should be erected at regular intervals on the weld mesh panels with words such as "Construction exclusion zone - Keep out".

Supervised demolition

Hard surfacing:
Removal of and or replacement of hard surfacing situated either partially or completely within the RPAs of retained trees shall be undertaken with care and under the direct on-site arboricultural supervision as these areas are likely to contain roots.
Where this is necessary the wearing course will be broken up using a hand held pneumatic breaker, hand tools and a wheel barrow to break up and remove the surfacing. If it is necessary to remove the sub base this is to be undertaken using hand tools such as a fork to loosen the material and removed using shovels and wheels barrows.
In some situations and at the discretion of the arborist it may be possible to use an excavator using a hydraulic breaker and suitably sized toothless grading bucket. If an excavator is to be used it must be situated outside of the RPAs, on top of the hard surfacing working away from the RPAs or from ground boarding.
Which ever system is used the is to be **NO** disturbance of the soil beneath. If roots are found they are to be covered over with damp hessian and a layer of either sharp sand, wood chip or top soil to prevent desiccation.
Structures:
Demolition of existing structures and foundations situated either partially or completely within RPAs of retained trees shall be undertaken with care and under the direct on-site arboricultural supervision as these areas are likely to contain roots.
Where it is necessary for the foundations to be removed they are to only be removed where critical to the proposed development and to the minimum depth required. The foundations will be broken up using a hand held pneumatic breaker, hand tools and a wheel barrow to break up and remove the surfacing. In some situations and at the discretion of the arborist it may be possible to use an excavator using a hydraulic breaker and suitably sized toothless grading bucket. If an excavator is to be used it must be situated outside of the RPAs, on top of the hard surfacing working away from the RPAs or from ground boarding. If it is likely that there will be any collapse of the soil within the rooting environment excavation is to be stopped immediately and the trench is to be shored up to prevent loss of the rooting environment.
Which ever system is used there is to be **NO** disturbance of the soil on the tree side of the foundations. If roots are found they are to be covered over with damp hessian and a layer of either sharp sand, wood chip or top soil to prevent desiccation.



Arboricultural Supervision

The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include:

1. Pre-commencement site meeting.
2. Location of protective measures.
3. Supervised demolition of the existing hard surfacing, kerb edging and foundations within and adjacent to the RPAs of tree numbers G1, G2, G3 and G4.
4. Any demolition and or excavations within or adjacent to RPAs, including foundations, hard surfacing or underground services (a non-exhaustive list).
5. Arboricultural sign off and removal of protective measures.

Arboricultural Method Statement

Please refer to Arbtech Consulting Ltd. Tree Schedule and Arboricultural Method Statement, for full details on all surveyed trees and how all aspects of the the development maybe implemented without detriment to retained trees.

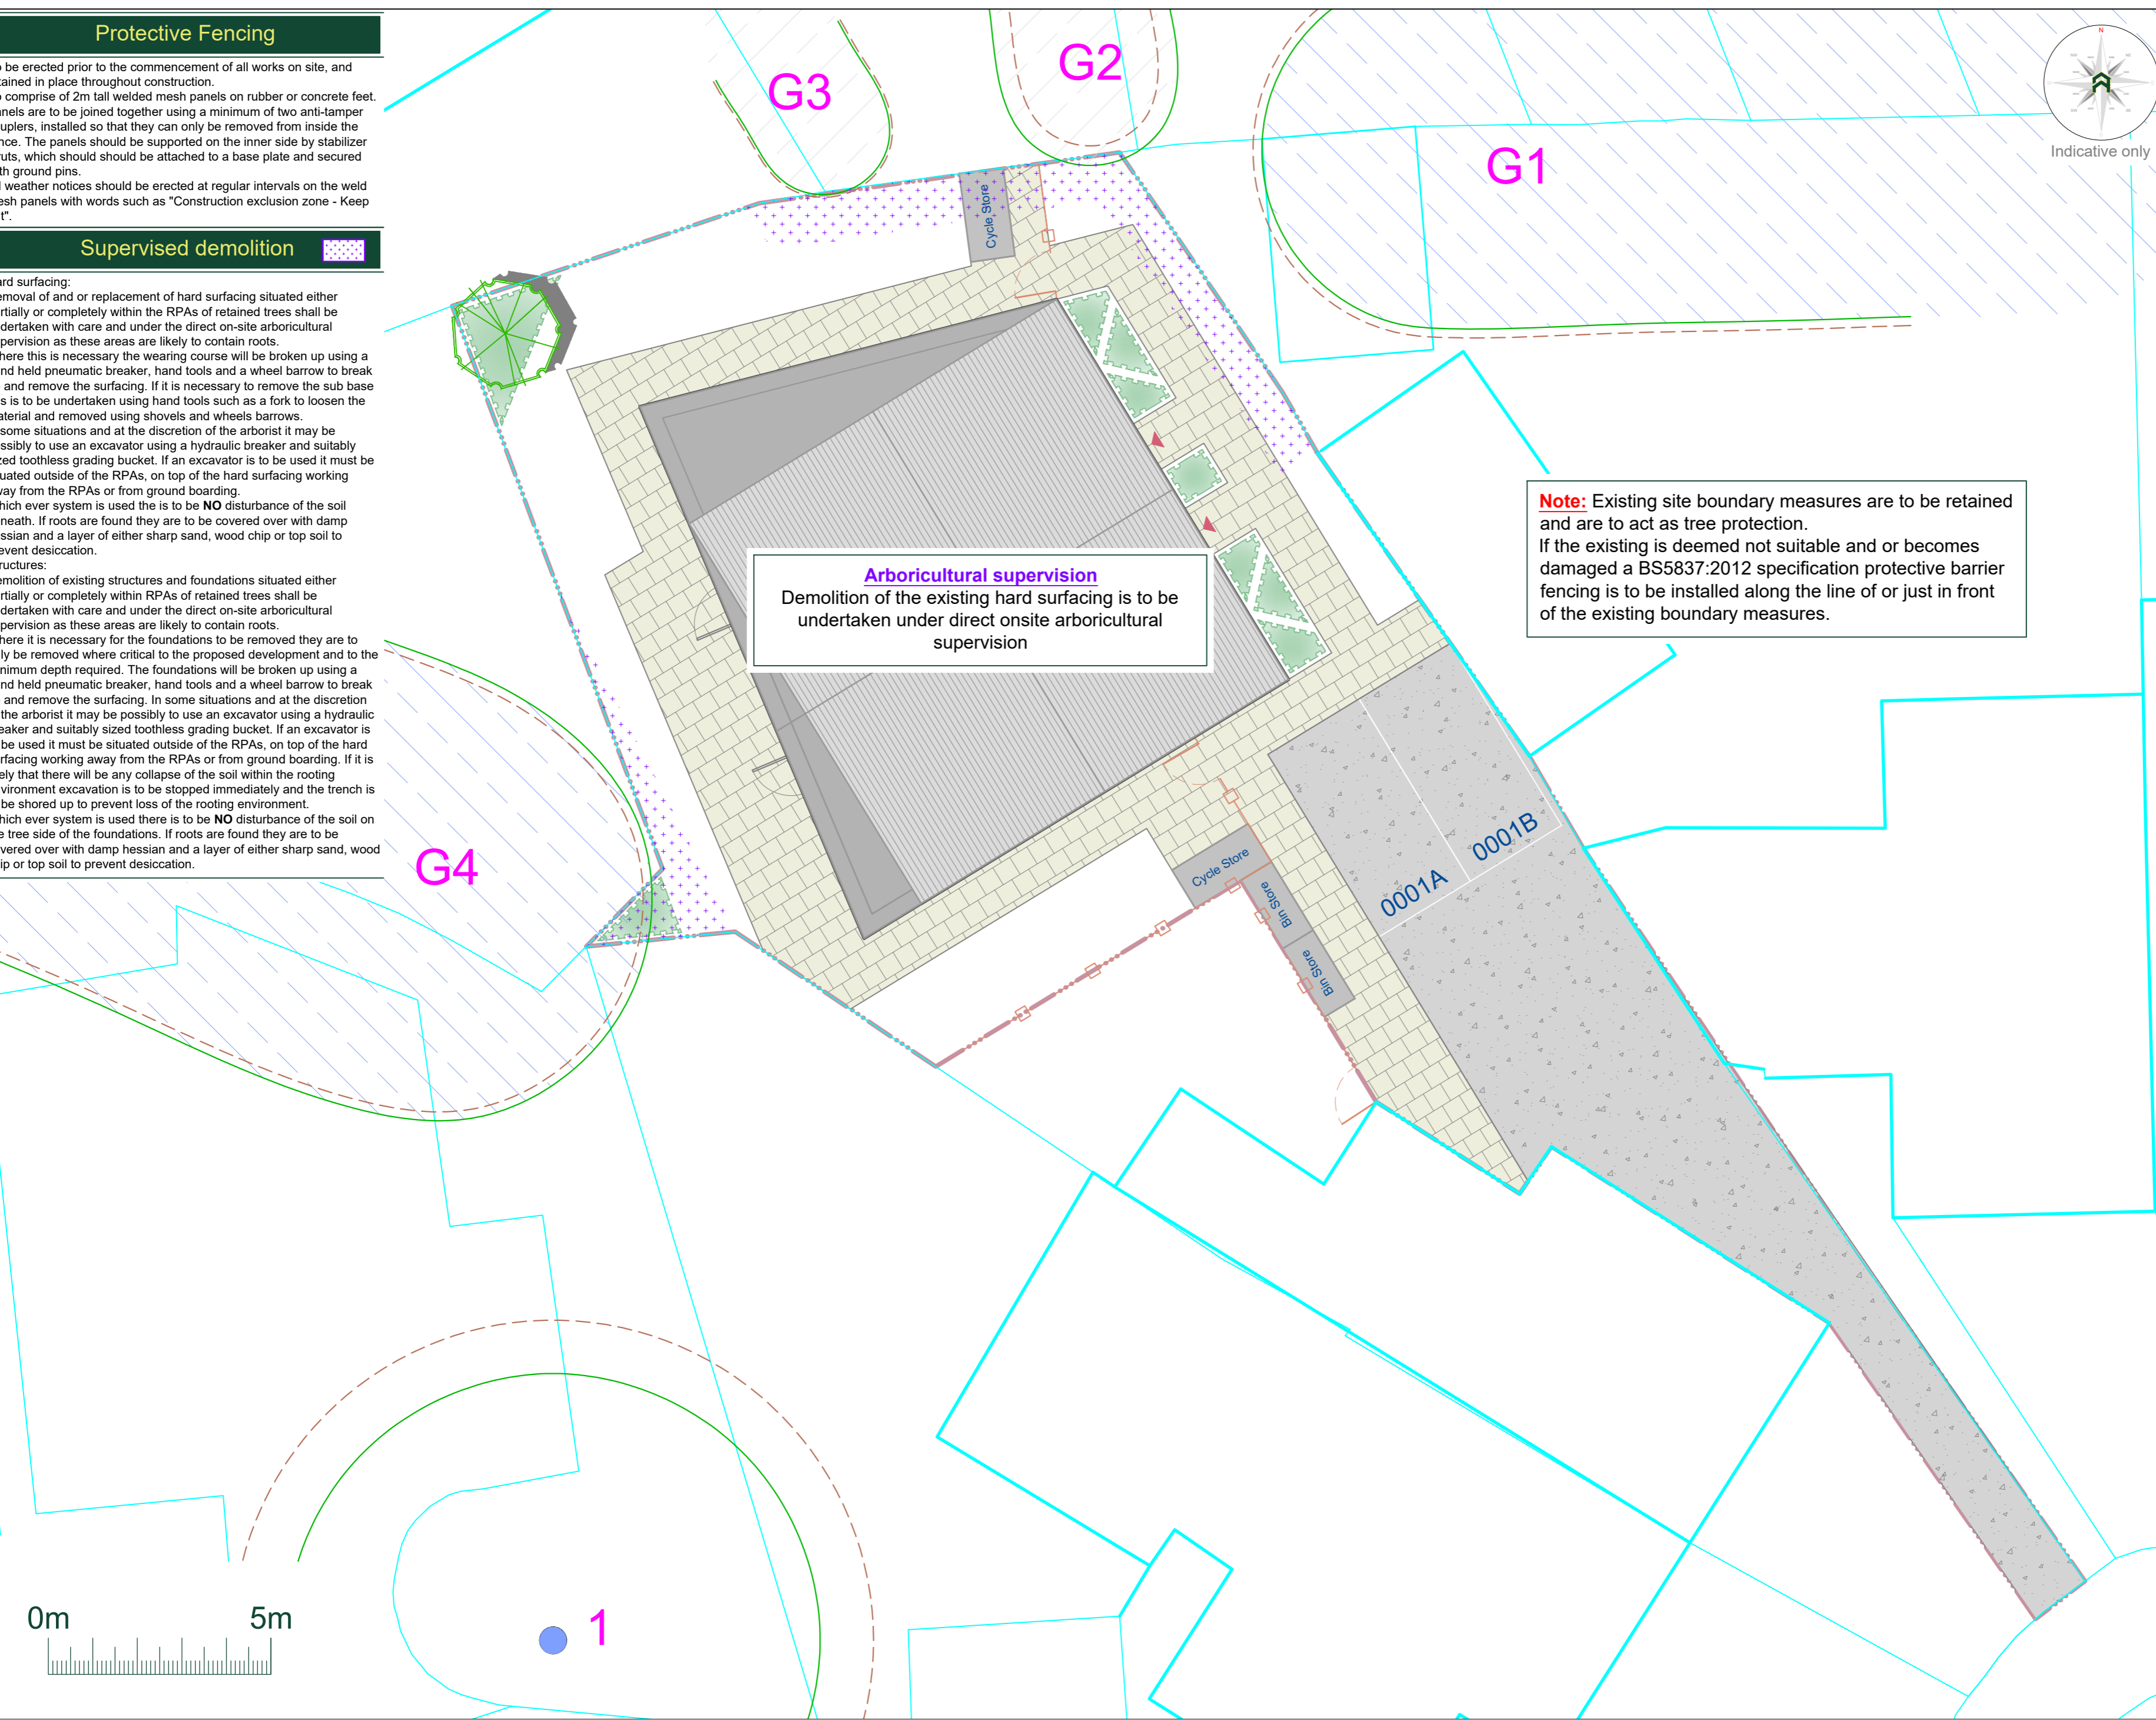

Arboricultural supervision
Demolition of the existing hard surfacing is to be undertaken under direct onsite arboricultural supervision

Note: Existing site boundary measures are to be retained and are to act as tree protection. If the existing is deemed not suitable and or becomes damaged a BS5837:2012 specification protective barrier fencing is to be installed along the line of or just in front of the existing boundary measures.



Unit 3, Well House Barns, Chester, CH4 0DH
<https://arbtech.co.uk>, 01244 661170

Project:	34a Drayton Gardens, West Drayton, UB7 7LG.		
Client:	Sazz Investments Limited		
Drawing:	Tree Protection Plan		
Based on:	A1442_(SK)010 C LDP-25-P297 1002		
Drawing No:	Arbtech TPP 01		
Date:	Scale:	Drawn:	
Feb 2026	1:200 @ A2	MGM	
Key:			
Tree Nos.:	1	Tree Canopies:	Trunks:
RPAs:	Category 'B' trees:	Category 'B' groups:	
Category 'C' groups:	Existing Site: (OS tile):	Arboricultural supervision - Demolition:	
<small>All dimensions should be checked on site. No dimensions are to be scaled from this drawing. Please notify us of any discrepancies found. Arbtech Consulting Ltd. cannot be held responsible for inaccuracies in the base drawing in which this plan is based. This drawing is designed to reflect the principles of the layout or design only, and relates only to the protection of retained trees. This drawing is not to be read as a definitive part of the engineering or construction designs or method statement. An architect or structural engineer should be contacted over any matters of construction, detailing or specification and for any standards or regulatory requirements relating to proposed structures, hard surfacing or underground services. This drawing was produced in colour - a monochrome copy should not be relied upon.</small>			
© Arbtech Consulting Ltd			

