


Rev:	Date:	Description:	By:
A	15/01/21	Initial fire strategy added	LDT
B	08/03/21	Reconfigured Nursery 1 and 2, along with Infant class 1 and surrounding support space. Entrance area reconfigured. Glazed panels added to Staff work areas and SEN Therapy. Toilets re-jigged to accommodate changes.	LDT
C	02/09/21	Internal Layout amended to fit previous layout by other contractor.	WEH
D	08/09/21	Few minor changes to the layout. Indicative ramps.	WEH
E	10/09/21	Internal amendments made to layout based on customer annotations	LDT
F	13/09/21	Minor amendment to WC / Interview / Repro and indicative ramps added to layout.	LDT
G	15/09/21	Removed counter 7 sink from hygiene room; relocated staff/acc WC from near nursery 1 to near infant class 5; relocated water fountain to outside staff/acc WC near infant class 6; added internal doors to cleaners cupboard, inbetween nursery 1 & 2 and WC's near nursery 2; swapped over the office/meeting room and sick bay; moved double door & wall up 1m north in the sub lobby; removed sliding hatch from sick bay; added extra sliding hatch to general office and moved existing sliding hatch down; moved double door inside the entrance lobby down; added steps to all ramps and made all ramps 1.8mm wide; removed link and doors from circulation 7 area.	LAH
H	16/09/21	Further minor amendment to WC / Interview / Repro.	LDT
I	27/09/21	Ramps / steps amended, minor tweak to sick bay, cloak rooms changed to group rooms	LDT
J	29/09/21	Ramps re-modelled in 3D and added to elevations	WEH
K	30/09/21	Ramps REMOVED to facilitate level access entry	LDT
L	07/10/21	Further minor amendment to Food Bay / Practical Resources & Hygiene Room	MTK
M	15/10/21	Dimensions, 30min & 60 min fire rated partitions added and Fire Rating annotations added.	MTK
N	21/10/21	Flooring Amendments, Fittings removed due to other contractors	WEH
O	03/11/21	6 x barrier mats added	MTK
P	24/11/21	Nursery doors changed to single, anti slip added to water fountains	LDT
Q	09/12/21	Window in Nursery 1 added, window in General Store removed. Minor amend to Food Bay flooring, barrier mats added to hall	LDT
R	22/12/21	Classroom doors made fully glazed and 'Titan' windows added	LDT
S	01/03/22	Flooring amended	BME
T	03/03/22	Added partition openings to nursery WCs, moved drinking fountain to Block A, IWB annotations added to Food Room & Studio, DIMS added for link doorsets, DIMS added to lobby areas, amended servery aperture, amended doorsets to Servery/Store to 926/926	BME

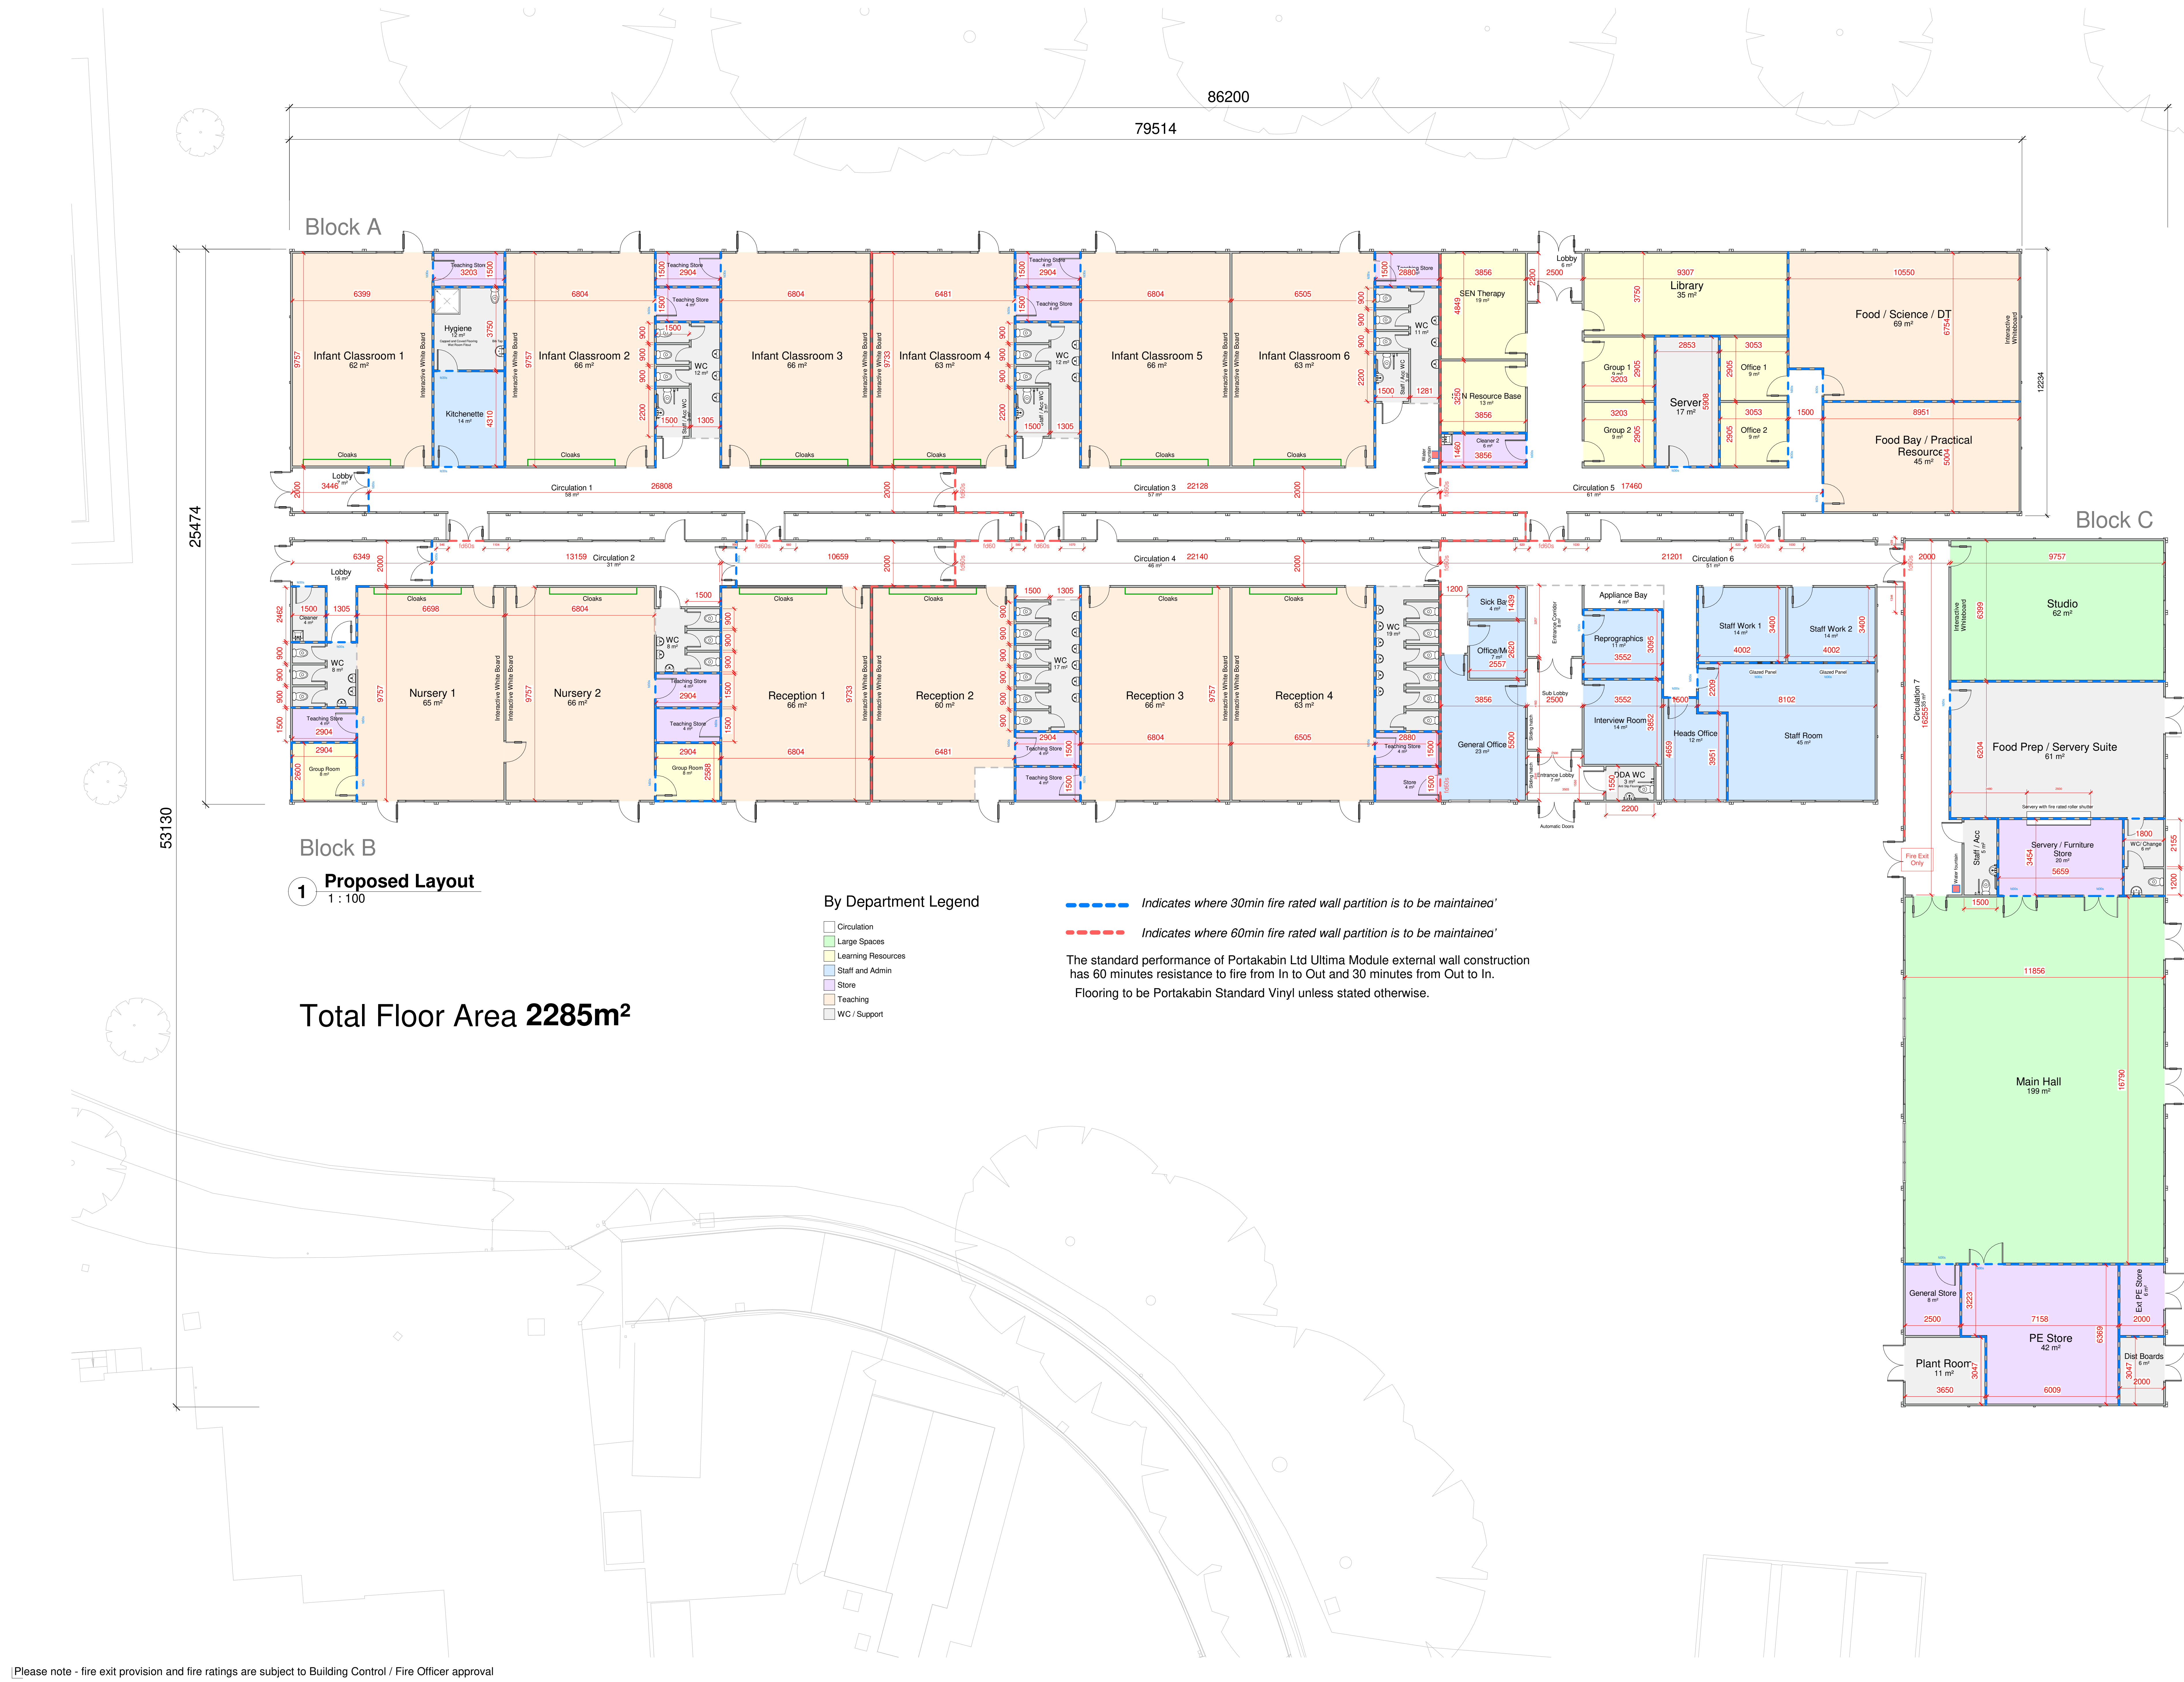

Please note - fire exit provision and fire ratings are subject to Building Control / Fire Officer approval

Standard floor loading is 3kN/m². Any loading imposed on a floor that is greater than 3kN/m² may require strengthening. Please contact your hire centre if you expect to exceed 3kN/m².

Please note that this and any accompanying drawing(s) are for illustrative purposes only and as such, the building shown may vary from the actual finished building on site.

The position of windows, external doors and electrical fixtures (if shown) are dependent on stock availability at time of order.

- EXTERNAL COLOUR SCHEME |**
- Ultima**
 - Walls** - Goosewing Grey - nearest BS ref 10 A 05
 - Vertical wall trim** - Goosewing Grey - nearest BS ref 10 A 05
 - Bottom wall trims** - White - nearest BS ref 00 E 55
 - Long wall fascias (covering wall)** - Goosewing Grey - nearest BS ref 10 A 05
 - Long wall fascia (covering beam)** - White - nearest BS ref 00 E 55
 - Short wall composite fascia** - Goosewing Grey - nearest BS ref 10 A 05
 - Roof** - White - nearest BS ref 00 E 55
 - External Skirt** - Goosewing Grey - nearest BS ref 10 A 05
 - Columns, external corners** - Grey - BS 4800 00 A 05
 - Columns, intermediate** - Grey - BS 4800 00 A 05
 - Windows** - Blue Grey - nearest BS 4800 18 B 29
 - Doors (insulated door)** - Slate Grey - nearest BS 18 B 25

Internal Portakabin Note
For connection details please see drawing DD0539

ZURICH **LABC** **BBA** **Constructionline** **CE** **ISO 9001** **ISO 14001** **ISO 45001** **BSI** **Safe** **HAS**

Portakabin

Portakabin Limited, New Lane, Huntingdon, York YO32 9PT, United Kingdom
+44 (0)1904 611655
portakabin.co.uk

Client: **Morgan Sindall Construction and Infrastructure**
Project: **Minet Infant & Junior School**
Title: **Proposed GA Layout // 58 x UK123 Ultima Modules**
Scale @ A3: **1 : 100** Date: **12/01/21** Drawn By: **LDT**
Drawing Number: **HD/12136/01** Rev: **T**
